# WHITE CREEK WIND PROJECT
# CONSTRUCTION SCHEDULE (87x2.3MW =200.1MW)
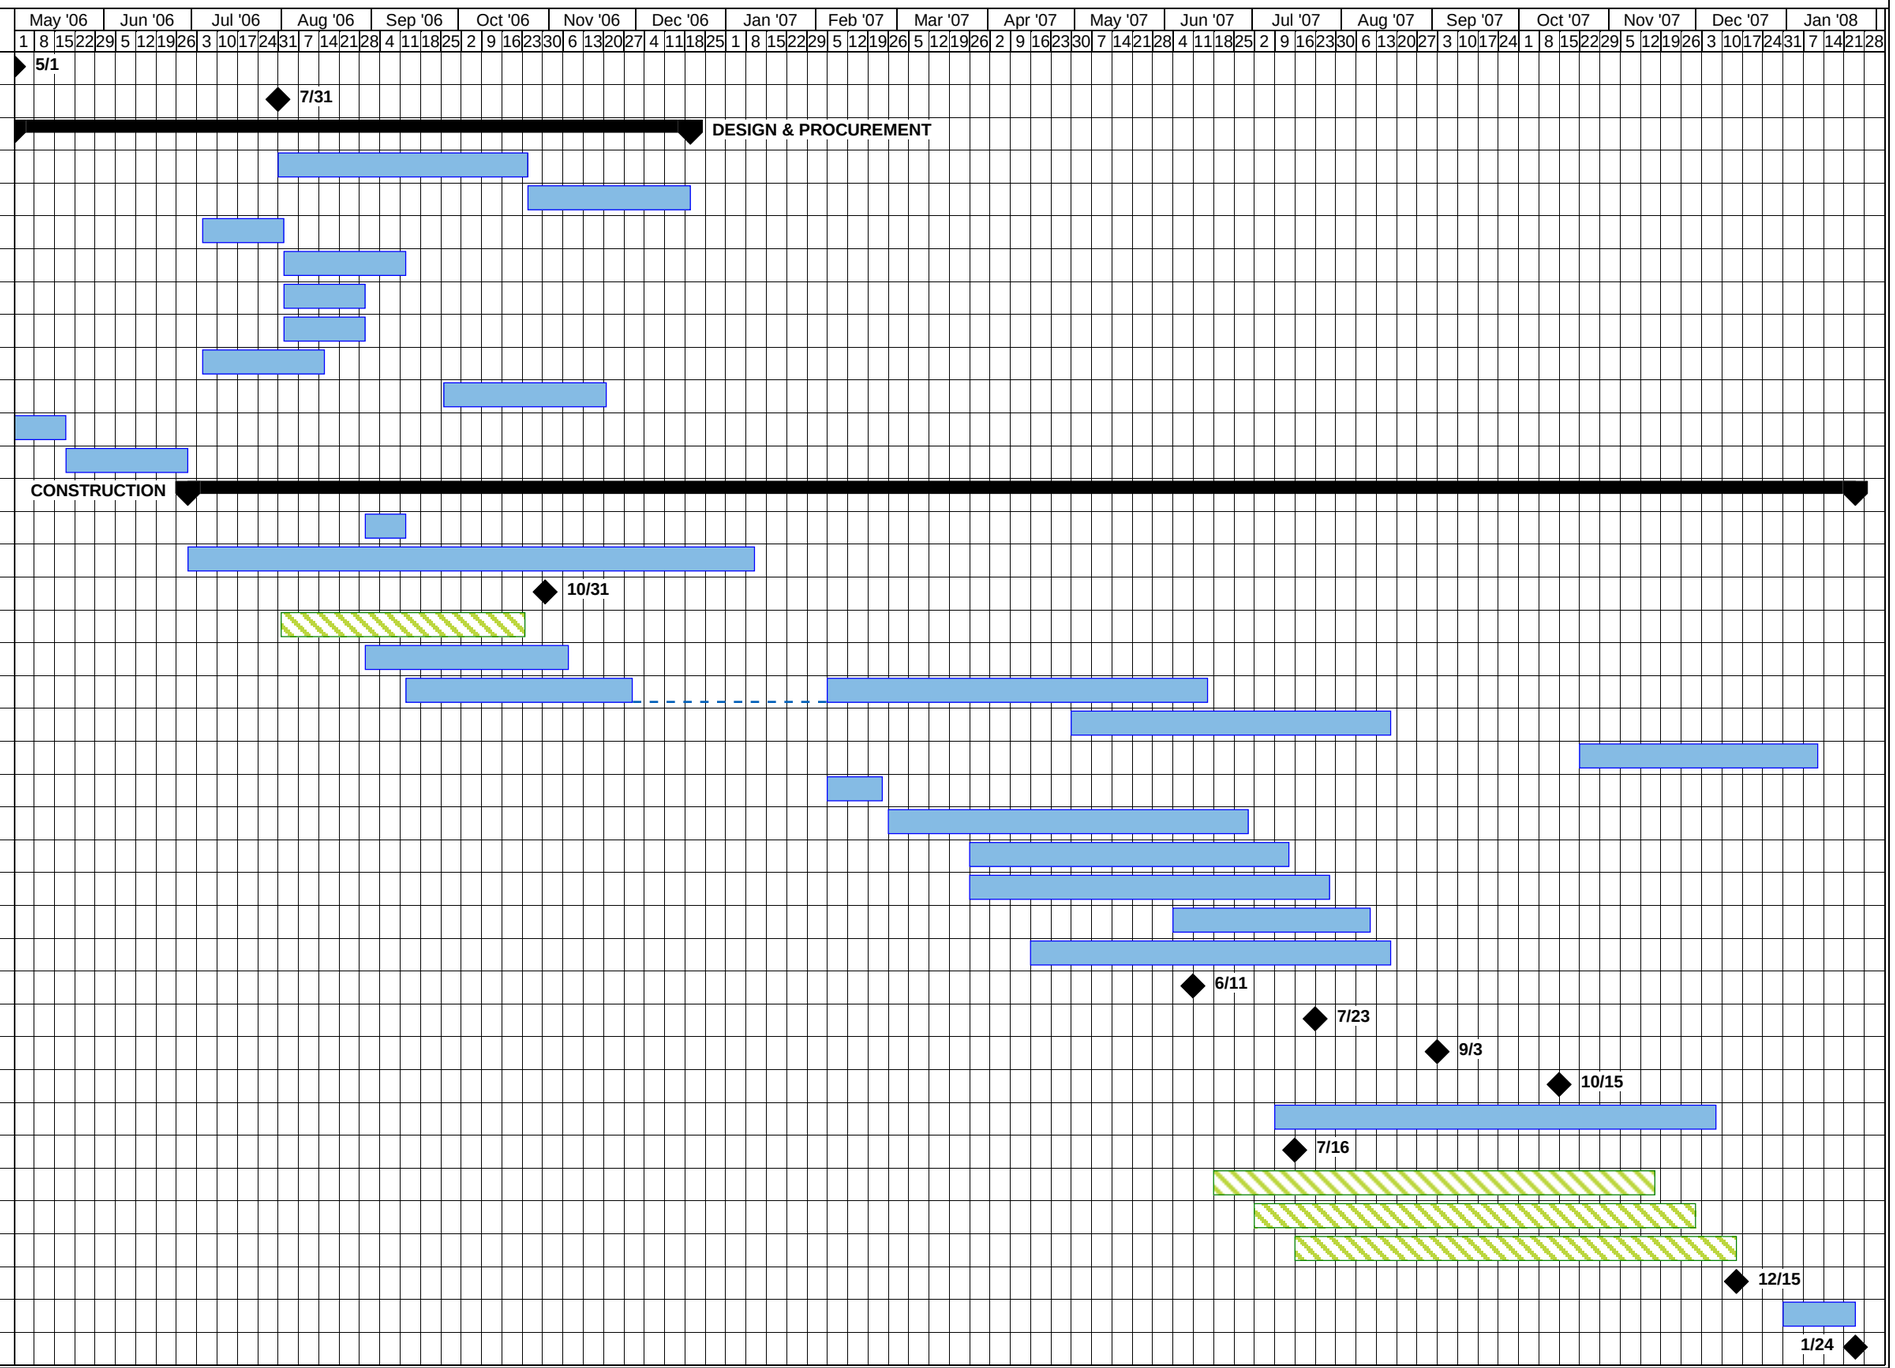
| ID | Task Name |
|---|---|
| 1 | **Sign BOP Contract** |
| 2 | **Notice to Proceed** |
| 3 | **DESIGN & PROCUREMENT** |
| 4 | Site investigation |
| 5 | WTG foundation design & building permits |
| 6 | Road design and SWPPP |
| 7 | NPDES permit (application + 30 day waiting period) |
| 8 | Other permits (CUP addendum, County ROW, road approach) |
| 9 | Other permits (utility crossings, clean air, sand and gravel) |
| 10 | Plans (weed control, erosion control, fire prevention) |
| 11 | MV cable & pad transformer design & procurement |
| 12 | O&M building - select subcontractor |
| 13 | O&M building - detailed design & building permit |
| 14 | **CONSTRUCTION** |
| 15 | Mobilise to site |
| 16 | O&M building - construction |
| 17 | Target date for O&M building to be weathertight |
| 18 | County Road upgrades (by others) |
| 19 | Roads - gravel crushing |
| 20 | Roads - Site roads & turbine pad construction |
| 21 | Roads - crane pad construction |
| 22 | Roads - final grading and site restoration |
| 23 | WTG foundations - set up batch plant |
| 24 | WTG foundations - construct foundations and transformer pads |
| 25 | Install pad-mount transformers |
| 26 | MV cable - trenching, laying and backfilling |
| 27 | MV cable - terminations and splices |
| 28 | LV cable - installation (WTG foundation to transformer pad) |
| 29 | Milestone date - 20 WTG foundation completions |
| 30 | Milestone date - 43 WTG foundation completions |
| 31 | Milestone date - 63 WTG foundation completions |
| 32 | Milestone date - 87 WTG foundation completions |
| 33 | LV cable - terminations in WTGs |
| 34 | Energize substation (by others) |
| 35 | Turbine deliveries (by others) |
| 36 | Turbine erection (by others) |
| 37 | Turbine commissioning (by others) |
| 38 | **Substantial Completion** |
| 39 | De-mobilise and clear site |
| 40 | **Final Completion** |
